Maidenhead Missing Links Programme

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**LEP Approval**	**2 days**	**Tue 06/11/18**	**Wed 07/11/18**	
2		Board Meeting/approval of Busin	0 days	Thu 31/01/19	Thu 31/01/19	
3		RBWM Commision Design	2 wks	Mon 04/02/19	Fri 15/02/19	2FS+2 days
4		**Preliminary Design**	**110 days**	**Mon 04/02/19**	**Fri 05/07/19**	
5		Commision topo of route	4 wks	Mon 04/02/19	Fri 01/03/19	3FS-10 days
6		C2 Statuatory Undertakers	1 wk	Mon 18/02/19	Fri 22/02/19	3
7		**Local modelling**	**55 days**	**Mon 18/02/19**	**Fri 03/05/19**	
8		traffic counts and video survey	20 days	Mon 18/02/19	Fri 15/03/19	3
9		Arcady models	25 days	Mon 11/03/19	Fri 12/04/19	8FS-5 days
10		Linsig models	15 days	Mon 18/03/19	Fri 05/04/19	8
11		Modelling report	5 days	Mon 15/04/19	Fri 19/04/19	9,10
12		Update Concept designs	10 days	Mon 22/04/19	Fri 03/05/19	11
13		**Preliminary design development**	**30 days**	**Mon 22/04/19**	**Fri 31/05/19**	**6,11**
14		Location 1: Braywick Roundabc	5 days	Mon 22/04/19	Fri 26/04/19	11
15		Location 2: A4 Castle Hill Roun	5 days	Mon 29/04/19	Fri 03/05/19	14
16		Lcoation 3: A4 Cookham Roun	5 days	Mon 06/05/19	Fri 10/05/19	15
17		Location 4: Oldfield Road	5 days	Mon 13/05/19	Fri 17/05/19	16
18		Location 5: Ray Mill West	5 days	Mon 20/05/19	Fri 24/05/19	17
19		Location 6: Stafferton Way Ro	5 days	Mon 27/05/19	Fri 31/05/19	18
20		Prepare Cost estimate	2 wks	Mon 27/05/19	Fri 07/06/19	18
21		Prepare Safety Audit Submission	1 day	Fri 31/05/19	Fri 31/05/19	19FS-1 day
22		Stage 1 Road Safety Audit	2 wks	Mon 03/06/19	Fri 14/06/19	21
23		RSA Designers Response	1 wk	Mon 17/06/19	Fri 21/06/19	22
24		RSA Client Response	1 wk	Mon 24/06/19	Fri 28/06/19	23
25		Update Preliminary design	1 wk	Mon 01/07/19	Fri 05/07/19	24
26		Review Business Case	1 wk	Mon 01/07/19	Fri 05/07/19	24
27		Design Approval	0 days	Fri 05/07/19	Fri 05/07/19	26
28		**Consultation**	**20 days**	**Mon 08/07/19**	**Fri 02/08/19**	
29		Public Consultation	4 wks	Mon 08/07/19	Fri 02/08/19	27
30		**Detailed Design**	**86 days**	**Mon 05/08/19**	**Tue 03/12/19**	
31		C3 Statutory Undertakers	10 days	Mon 05/08/19	Fri 16/08/19	29
32		Location 1: Braywick Roundabou	15 days	Mon 19/08/19	Fri 06/09/19	31
33		Location 2: A4 Castle Hill Rounda	15 days	Mon 19/08/19	Fri 06/09/19	31
34		Lcoation 3: A4 Cookham Roundal	15 days	Mon 09/09/19	Fri 27/09/19	32
35		Location 4: Oldfield Road	15 days	Mon 09/09/19	Fri 27/09/19	32
36		Location 5: Ray Mill West	15 days	Mon 30/09/19	Fri 18/10/19	34
37		Location 6: Stafferton Way Roun	15 days	Mon 30/09/19	Fri 18/10/19	34
38		C4 Statutory Undertakers	20 days	Tue 01/10/19	Mon 28/10/19	37FS-15 days
39		Specification Document	2 wks	Mon 21/10/19	Fri 01/11/19	37
40		Stage 2 Road Safety Audit	2 wks	Mon 21/10/19	Fri 01/11/19	37
41		RSA Designers Response	1 wk	Mon 04/11/19	Fri 08/11/19	40
42		RSA Client Response	1 wk	Mon 11/11/19	Fri 15/11/19	41
43		Update plans	2 days	Mon 18/11/19	Tue 19/11/19	42
44		Review and Approvals	3 days	Wed 20/11/19	Fri 22/11/19	43
45		Detailed Design Sign Off	0 days	Tue 03/12/19	Tue 03/12/19	44
46		Pre construction information pack	5 days	Tue 26/11/19	Mon 02/12/19	43
47		Procurement	20 days	Tue 03/12/19	Mon 30/12/19	46
48		Mobilisation	10 days	Tue 31/12/19	Mon 13/01/20	47
49		**Construction**	**155 days**	**Tue 14/01/20**	**Mon 17/08/20**	
50		Location 1: Braywick Roundabou	30 days	Tue 14/01/20	Mon 24/02/20	48
51		Location 2: A4 Castle Hill Rounda	30 days	Tue 28/04/20	Mon 08/06/20	53FS-5 days
52		Lcoation 3: A4 Cookham Roundal	30 days	Tue 02/06/20	Mon 13/07/20	51FS-5 days
53		Location 4: Oldfield Road	30 days	Tue 24/03/20	Mon 04/05/20	55FS-5 days
54		Location 5: Ray Mill West	30 days	Tue 07/07/20	Mon 17/08/20	52FS-5 days
55		Location 6: Stafferton Way Roun	30 days	Tue 18/02/20	Mon 30/03/20	50FS-5 days

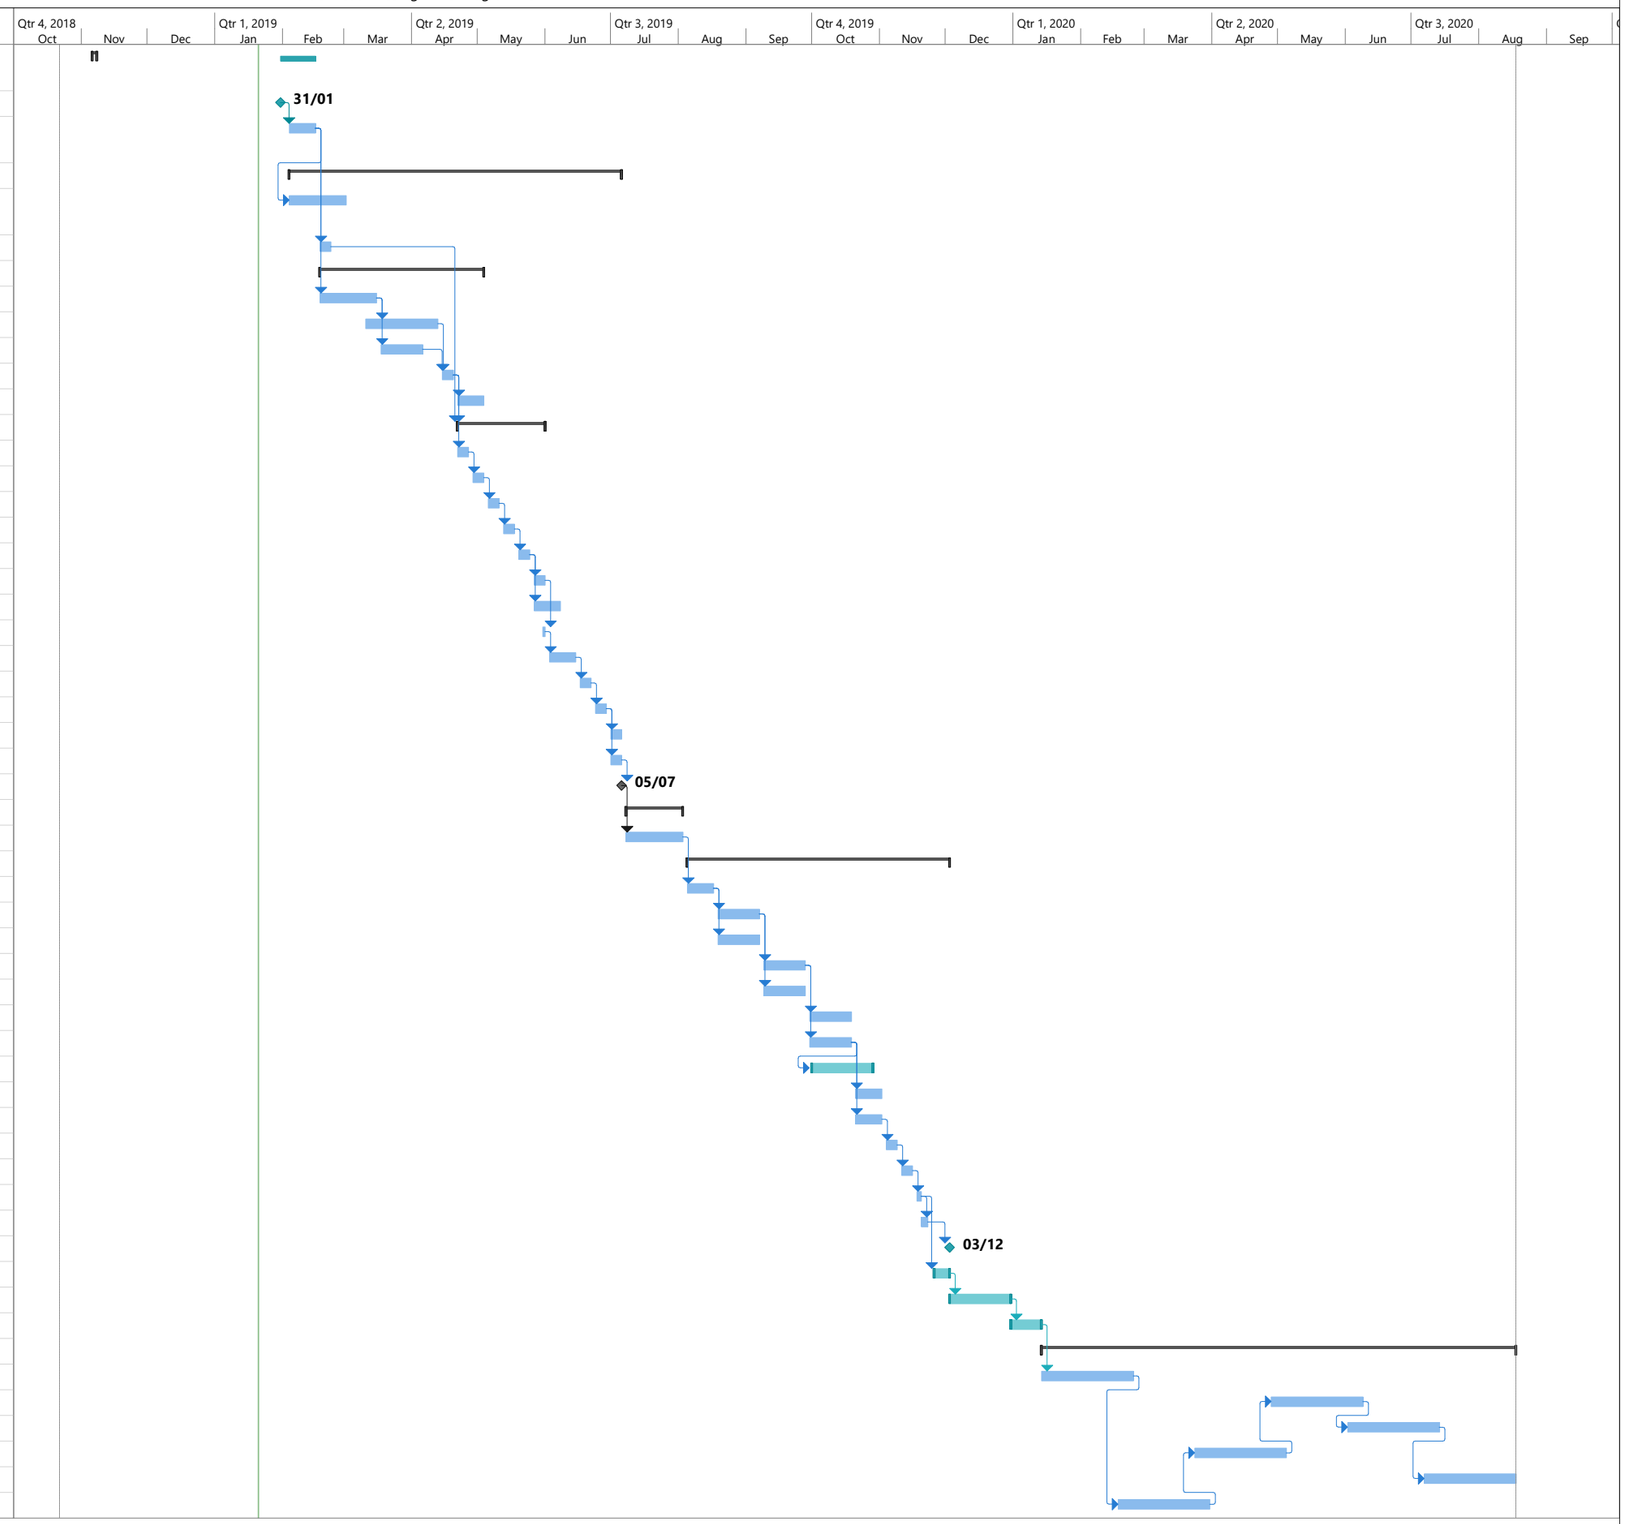

Project: 2018 11 15 MML Prelim
Date: Mon 21/01/19

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
